



BOND PROGRAM

AUSTIN ISD 2022

May 2026

Design & Construction Updates



Agenda



AGENDA

AGENDA ITEM	Presenter	START	DURATION
Call to Order	Co-Chairs	6:00 p.m.	5 min
Public Comment (2 mins per comment, max 10 mins)	Alleigh Gregson	6:05 p.m.	10 min
Approval of Minutes: April 10 (Voting Item)	Co-Chairs	6:15 p.m.	5 min
Communications <ul style="list-style-type: none"> Media/Events CAT & Community Meetings 	Melissa Laursen	6:20 p.m.	5 min
Finance <ul style="list-style-type: none"> 2017 Financials 2022 Financials 	Angela Mendez	6:25 p.m.	10 min
CMD 2022 <u>Modernization/Comprehensive</u> Projects Updates including: <ul style="list-style-type: none"> Safety Report Worker Protection Report Mendez MS Sims ES (Alternative Learning Center) Third-party educational contractors at bond-funded campuses Yellow Jacket Stadium Oak Springs ES 	Melfi Brunson Travis Neumann Michael Mann & Project Managers	6:35 p.m.	45 min
CMD 2022 <u>Targeted</u> Projects Updates <ul style="list-style-type: none"> Kealing MS Fencing Turf & Track Projects 	CMD Staff	7:20 p.m.	10 min
CMD 2017 Bond Projects Updates including: <ul style="list-style-type: none"> Eastside ECHS 	CMD Staff	7:30 p.m.	5 min
CBOC Committee Operations <ul style="list-style-type: none"> Survey Update Bylaws Revision Update SPED Camera Board Response 	Co-Chairs	7:35 p.m.	20 min
Future Items for Discussion	Co-Chairs	7:55 p.m.	5 min
Adjourn	Co-Chairs	8:00 p.m.	--

Public Comment

All regular and plenary meetings of AISD advisory bodies are open to the public.

Members of the public may join CBOC meetings in-person and provide comments during the meeting or directly to the shared CBOC inbox before the meeting begins.

Email Address: cbocinternalinfo@austinisd.org

Five minutes of Public Comment may be read (maximum of 10 mins depending on sign-ups, no more than 2 mins per comment).



BOND
PROGRAM
AUSTIN ISD 2022

APPROVAL OF MINUTES

UP NEXT:



**BOND
PROGRAM**
AUSTIN ISD 2022



BOND COMMUNICATIONS

Austin ISD Bond Media Highlights

We're keeping the community updated on the ongoing bond progress through news stories and social media posts. Check out the latest below.

Media Engagement

- [KXAN Harris Grand Opening](#)
- [Austin Current: Harris Grand Opening](#)

Social Media

- **Follow us on Instagram: @austinisdbond**
- [Burnet Middle School Update](#)
- [Harris Grand Opening Invitation](#)
- [Harris Grand Opening Livestream](#)
- [CMD Staff vs. Students Flag Football Game](#)

Construction update videos can be found on the [2022 Bond website](#).



Harris Elementary Grand Opening Celebration

Social Media Highlight



CMD Staff vs. Students
7 V 7 Flag Football Game

CAT Meetings & Upcoming Events

- 4/30: Northeast CAT #18 (5:30 pm)
- 5/14: Burnet MS (11 am - 1:30 pm)
- 5/14: Oak Springs/Blackshear CAT 18 (3:30 pm)
- 5/15: CAF CAT #16, Metz 113 (11 am - 12:30 pm)
- 5/20: Andrews ES Dirt Turning (10 am - 11:00 am)
- 5/20: Hill CAT #12 (3:30 pm)
- 5/21: Oak Springs/Blackshear CAT 19 (3:30 pm)

All meetings are open to the public and posted to the [Bond calendar](#).



Travis ECHS Construction Community Meeting

UP NEXT:



**BOND
PROGRAM**
AUSTIN ISD 2022

BOND FINANCIALS

2017 Bond Financials



Bond amount authorized by voters on November 7, 2017: **\$1,050,984,000**

Actually Spent

\$ 1,058,147,477

**Total Projected
Costs & Current
Commitments**

\$ 2,678,782

**Bond Program
Available Balance
After Commitments**

\$ (9,842,259)

*Please see file: 2017 Bond Program Financials

2022 Bond Financials

Proposition A (General Purpose)



Bond amount authorized by voters on November 8, 2022: **\$2,316,025,000**

Actually Spent

\$ 913,048,382

**Total Projected
Costs & Current
Commitments**

\$ 830,934,420

**Bond Program
Available Balance
After Commitments**

\$ 572,042,198

*Please see file: 2022 Bond Program Financials

2022 Bond Financials

Proposition B (Technology)



Bond amount authorized by voters on November 8, 2022: **\$75,541,000**

Actually Spent

\$ 36,919,997

Total Projected Costs & Current Commitments

\$ 4,463,453

Bond Program Available Balance After Commitments

\$ 34,157,550

*Please see file: 2022 Bond Program Financials

2022 Bond Financials

Proposition C (Stadiums & Athletic Complexes)



Bond amount authorized by voters on November 8, 2022: **\$47,434,000**

Actually Spent

\$ 999,481

**Total Projected
Costs & Current
Commitments**

\$ 2,356,947

**Bond Program
Available Balance
After Commitments**

\$ 44,077,572

*Please see file: 2022 Bond Program Financials

UP NEXT:











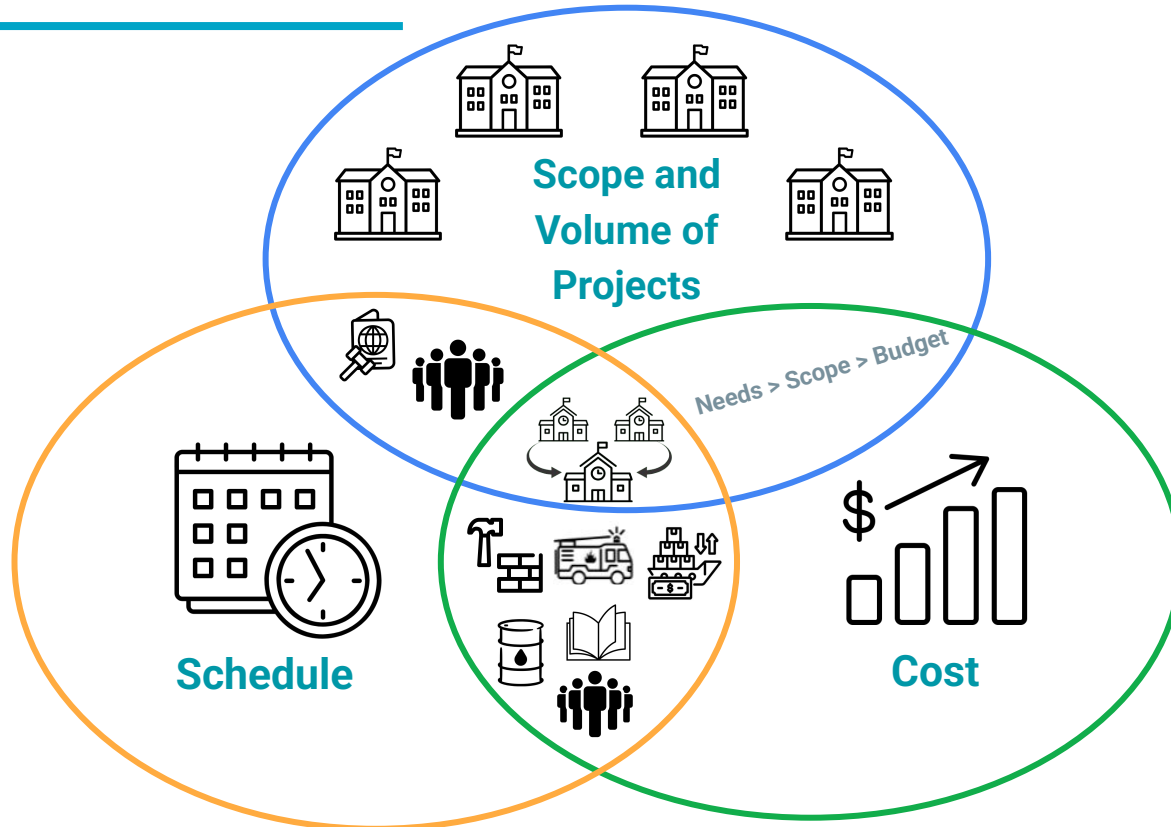
BOND
PROGRAM
AUSTIN ISD 2022

**2022 BOND
MODERNIZATION/COMPREHENSIVE PROJECTS**

Negotiations	Pre-Design	Schematic Design	Design Development	Construction Documents	Construction	
		<ul style="list-style-type: none"> ◇ Burger Athletic Complex ◇ Noack Sports Complex © ◇ Yellow Jacket Stadium (A) 	<ul style="list-style-type: none"> ◇ Delco Activity Center (C) ▲ Hill ES (A) 	<ul style="list-style-type: none"> ▲ Andrews ES (A) ▲ O. Henry MS (A) ◇ Nelson Field (C) ▲ Wooldridge ES (A) ◇ Nelson Bus Terminal (A) 	<ul style="list-style-type: none"> ▲ *Travis ECHS (A) ▲ *Akins ECHS (A) ▲ *LBJ ECHS (A) ▲ *Houston ES (A) ▲ *Pecan Springs ES (A) ▲ *Austin HS (A) ▲ *Linder ES (A) ▲ *Allison ES (A) ▲ *Burnet MS (A) ▲ Oak Springs ES (A) 	<ul style="list-style-type: none"> ◇ Northeast ECHS (A) ◇ McCallum (A) ◇ Anderson HS (A) ◇ Crockett ECHS (A) ◇ *Langford ES (A) ◇ *Sadler Means YWLA (A) ◇ *Clifton CDS (A) ◇ Dobie MS (A) ◇ Navarro ECHS (A) ◇ Mendez MS (A)
<div style="background-color: #002060; color: white; padding: 5px; text-align: center; font-weight: bold;">ICON KEY</div> <ul style="list-style-type: none"> – Propositions: (A) Prop. A (B) Prop. B (C) Prop. C – Program Managers: ▲ AECOM ◇ Vanir/STV – Final GMP * 					Transition to Operation	
					<ul style="list-style-type: none"> ▲ *Cook ES (A) ▲ *Oak Hill ES (A) ▲ *Odom ES (A) ▲ *Williams ES (A) ▲ *Wooten ES (A) ▲ *Harris ES (A) 	

Program-Wide Challenges & Strategies

-  Project
-  People/Labor
-  Schedule
-  Balance
-  Materials
-  Cost/Escalation
-  Tariffs
-  New Building Code
-  AFD Changes
-  Consolidations
-  Work Labor Risks
-  War Effects



Contingency & Escalation Use Update

Current reporting for Prop A

**Note: Information presented here is intended to communicate recent needs for contingency and escalation funds and is not intended to be a substitute for the financial reports provided. Interest balances are provided in monthly reporting.*

Bond Program	Original Balance	Balance as of March (to match financial report)	Previous Balance (as of 3/31)	Current balance (as of 4/30)	2022 Interest Used
Contingency	\$129,093,277	\$28,502,019	\$770,214	\$1,363,541	n/a
Escalation	\$270,516,395	\$50,076,898	\$64,159,352	\$69,995,148	n/a
Interest	n/a	n/a	n/a	n/a	\$57,776,642 (none used in the past month)

Contingency:

- \$593,327 - Unused balance of procurement staff aug PO moved to program contingency

Escalation:

- \$3,735,828 - Money moved out of projects at campuses that are closing
- \$7,000,000 - Unused balance from Covington project moved into escalation
- (\$650,605) - To NECHS for City of Austin fee-in-lieu for water quality pond
- (\$2,259,932) - Additional funding needed to complete security fencing
- (\$1,800,564) - To Austin HS project for City of Austin fee-in-lieu for water quality pond, and Soft Costs
- (\$741,000) - For refresh at Rodriguez ES as a receiving campus
- \$122,311 - Money moved out of Cowan ES project for closeout
- \$429,758 - Unused bond bus funds moved to Nelson Bus Terminal modernization

Interest Usage:

- No spend since the January CBOC meeting

Contingency & Escalation Use Report

Current reporting for Prop C

**Note: Information presented here is intended to communicate recent needs for contingency and escalation funds and is not intended to be a substitute for the financial reports provided.*

Bond Program	Original Balance	Balance as of March (to match financial report)	Previous Balance (as of 3/31)	Current Balance (as of 4/30)	2022 Interest Used
Contingency	\$2,834,978	\$2,834,978	\$2,834,978	\$4,746,682	n/a
Escalation	\$5,669,955	\$5,669,955	\$5,669,955	\$5,669,955	n/a
Interest	n/a	n/a	n/a	n/a	\$5,960,742 (none used in the past month)

Contingency Usage:

- \$1,911,704 - Moved money from accounts that are not needed (ex: rental: land and buildings, contracted services, etc.) to Program Contingency.

Escalation Usage:


- CAF CAT in discussions on how best to allocate escalation funds across the Prop C projects.

Interest Usage:

- N/A

▲ Mendez Middle School


Phased Modernization | Prop. A



Scan the QR code to see the campus project page

[Project Fact Sheet](#)

PHASE: SCHEMATIC DESIGN | OPEN: AUG 2027 | SWING: Y (ON SITE) | ON BUDGET: Y

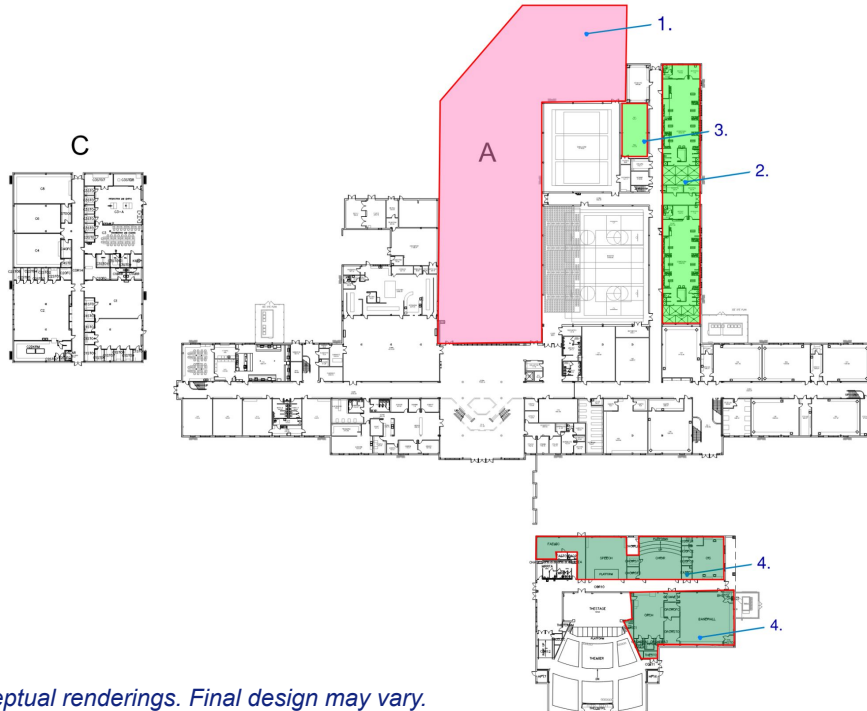

Project Overview:

Phase 1 Summer 2025 (Complete)


Secure Vestibule, ALC work, partial re-roof.

Phase 2

1. Outdoor learning and courtyard improvements.
2. Locker room renovations - new shower and toilet stalls.
3. Weight room relocation.
4. Fine arts renovation - Flooring, ceiling, lights, m paint, doors, duct work, FF&E.

**Conceptual renderings. Final design may vary.*

Alternative Learning Center: Mendez Site



Scan the QR code to see
the campus project page

[Project Fact Sheet](#)

Project Highlights:

- ALC will co-locate at Mendez MS with:
 - 3rd Future Charter serving Mendez MS students - Separated within the main building
 - Juvenile Justice Alternative Education Program (JJAEP) - In portables
 - CIS ASPIRE Family Literacy Program - In separate building
 - Love Hub - In separate building
- 2022 Bond Book Amount and Breakdown:
 - Total Bond Book = \$724,000
 - Technology (Prop C) = \$102,041
 - Program Management (Prop A) = \$128,494
 - ALC Targeted Work (Prop A) = \$493,465
 - \$493,465 from ALC Bond funds allocated for site preparation at Mendez
 - Includes secure vestibule, HVAC improvements, and other building repairs as well as secure separation
 - Dedicated classrooms, drop-off/pick-up zones, restrooms, and gym
 - Separated and dedicated front office space

**Pulled from: September 9,
2025 CBOC Presentation**

▲ Sims Elementary School



Sims Elementary will house ALC/JJAEP now that Andrews ES is swinging to Winn ES during their modernization project. To accommodate ALC/JJAEP at Sims the following work was completed:

Campus Preparation (Harris ES Move-Out)


- Building cleared of furniture and equipment; only requested items remain
- Portables removed; Connex units cleared, pending removal

Classroom & Storage Modifications

- Classroom divider walls installed in Buildings A and E:
 - Building A: between Rooms 203 & 205, and 204 & 206
 - Building E: between Rooms 103 & 105, and 104 & 106
- Shelving removed from all storage rooms
- Facility Maintenance staff finalizing minor repairs in select areas

Funding & Move Coordination

- No bond funds used
- [Space relocation plan](#) approved by both principals (J. Hodges–ALC; Kim Andersen–JJAEP)
- ALC/JJAEP move from Mendez to Sims scheduled for June 2026

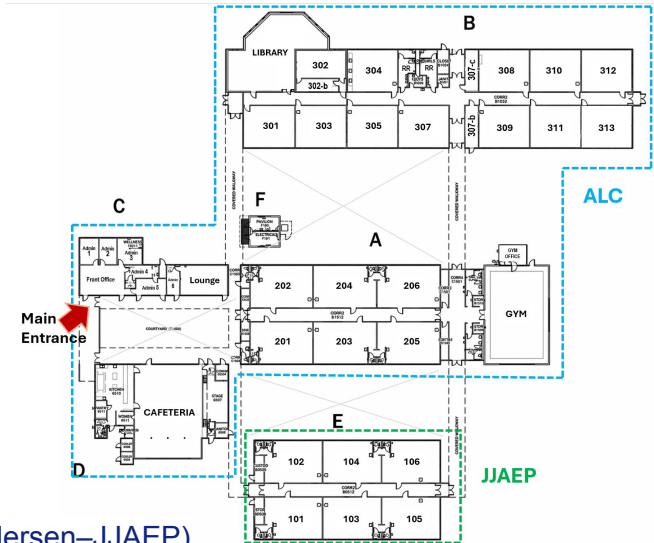

*Conceptual renderings. Final design may vary.

Third-Party Educational Contractors

(Texas Senate Bill 1882)

Mendez MS

- Previously: During the 1882 partnership at Mendez portions of the Phase Modernization scope were designed but not constructed because certain Fine Arts and related instructional spaces were not required under the partner program model. No bond scope was removed or reduced from the approved modernization program.
- Currently: Campus is transitioning from 1882 partnership model back to a AISD-operated campus. Remaining modernization work is now resuming and includes completion of Fine Arts improvements and remaining Phase Modernization items scheduled for Fall 2026.

Burnet MS

- Previously: During design Burnet MS was an AISD-operated campus and was designed as a fully modernization through new construction.
- Currently: Campus is transitioning into an 1882 partnership with a third-party educational contractor. No bond scope is being removed or reduced from the approved modernization project.

Dobie MS


- Previously: During design Dobie MS was an AISD-operated campus and was designed as a phased modernization.
- Currently: Campus is transitioning into an 1882 partnership model to third-party educational contractor. No bond scope is being removed or reduced from the approved modernization project.

Webb MS

- Previously: Webb MS has been an AISD-operated campus and is scheduled to receive targeted projects.
- Currently: Campus is transitioning into an 1882 partnership with a third-party educational contractor. No bond scope is being removed or reduced from the approved targeted projects.

Yellow Jacket Stadium

Phased Modernization | Prop. A



Scan the QR code to see the campus project page

[Project Fact Sheet](#)

PHASE: SCHEMATIC DESIGN | OPEN: MAR 2029 | SWING: Y (ON SITE) | ON BUDGET: Y

CAMPUS CONCEPT PLAN

- 1 Turf Installation - 100,200sqft
- 2 New WQ Pond + Underground Detention Area
- 3 Track Rebuild
- 4 New Digital Scoreboard +Time Clock
- 5 Upgrade to Field Lighting
- 6 Historic Fieldhouse Renovation
- 7 Historic Ticket Booth Restoration
- 8 New Visitor's Fieldhouse - 2,500sqft
- 9 High Jump Area
- 10 NFHS Long Jump and Triple Jump - 147' Runway
- 11 New Bleachers + Storage + Additional Restrooms
 - 3,500 Seats
 - Ramp Relocation
 - New 2,000sqft Restroom Facility
- 12 New Press Box - 2,000sqft
- 13 New Entry Portal
- 14 Historic Concessions Restoration
- 15 (2) New Field Lighting
- 16 Existing Field House to Remain
- 17 Existing Concessions Building to Remain
- 18 Update Site Signage
- 19 New Interior Fencing




2022 PROJECT SCOPE

1. Upgrade existing fieldhouse lockers to allow for visiting teams to have space.
2. Renovate level 1 of historic fieldhouse.
3. Restore historic ticket booth.
4. New Pressbox 250 square feet.
5. Re-grade and re-sod upper practice field.
6. New Discus area.
7. New High Jump area.
8. New long and triple jump.
9. New pole vault.
10. New field turf.
11. Track re-surfacing.
12. New shot put.
13. Increase bleacher seating to 750 seats.
14. New digital scoreboard and timeclock
15. New entry portal with historical elements.
16. New interior fencing to separate spectators from student athletes.
17. Marquee sign
18. Upgrade field lighting to LED, improve lighting at the ends of the track.
19. New water quality pond with underground detention.

*Conceptual renderings. Final design may vary.

Yellow Jacket Stadium


Modernization | Prop. C



Scan the QR code to see the campus project page


[Project Fact Sheet](#)

PHASE: SCHEMATIC DESIGN | OPEN: MAR 2029 | SWING: Y (ON SITE) | ON BUDGET: Y

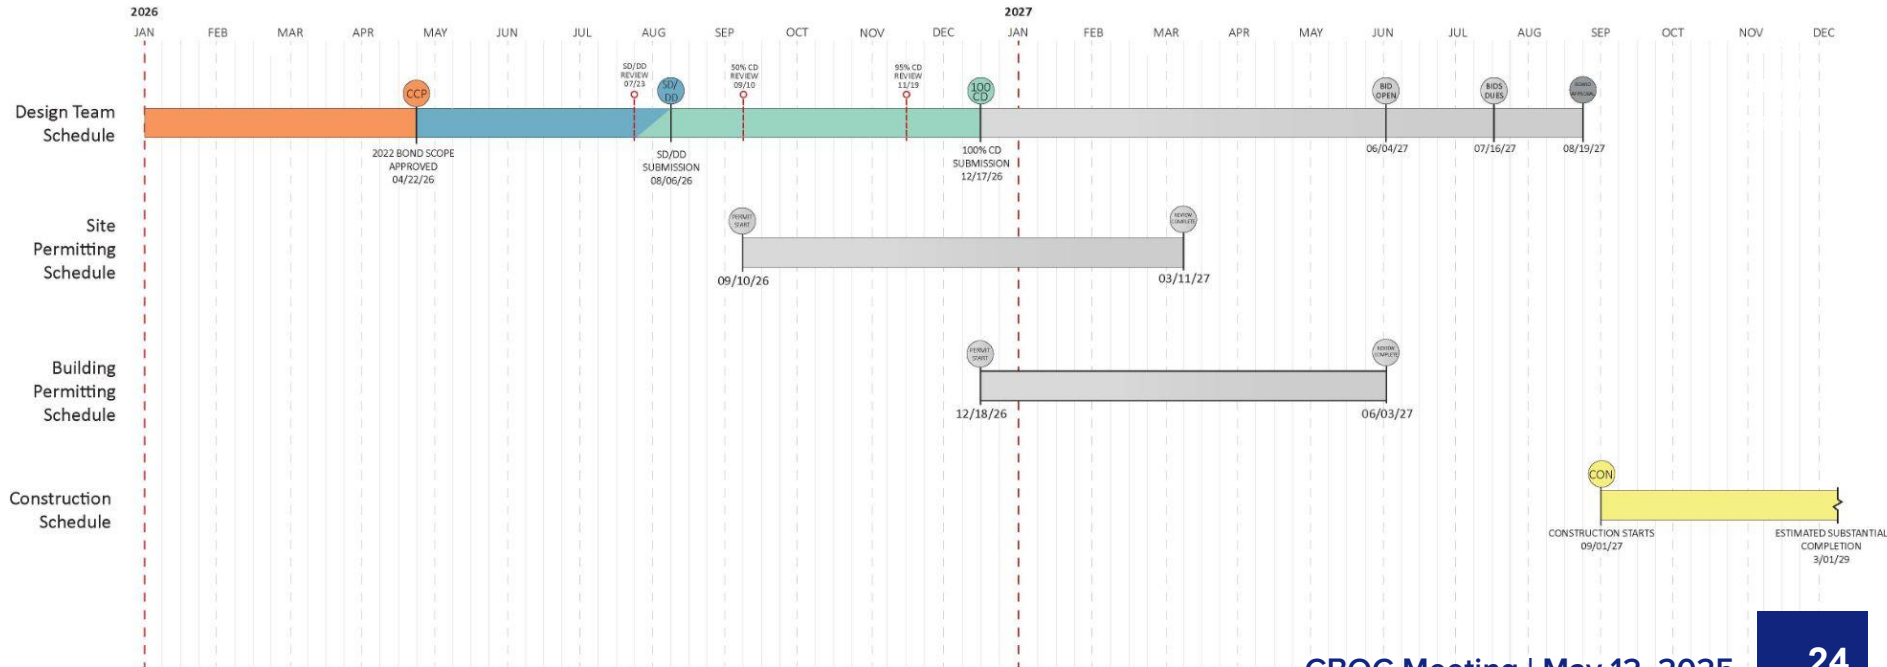

◆ Oak Springs Elementary School

Modernization | Prop. A




Scan the QR code to see the campus project page

[Project Fact Sheet](#)

PHASE: SCHEMATIC DESIGN | OPEN: JAN 2028 | SWING: N (ON SITE) | ON BUDGET: Y

Project Overview:

- Work put on hold due to consolidation. Work recently re-started
- Combined Blackshear and Oak Springs CAT meeting being held Thursday 5/14/2026.
- Community meeting planning is underway.
- Preliminary planning has occurred to adjust spaces inside the building footprint to accommodate Blackshear Fine Arts programs. The team will review those preliminary thoughts with the CAT on Thursday.
- Project Schedule is under review and a NSC will be forthcoming.

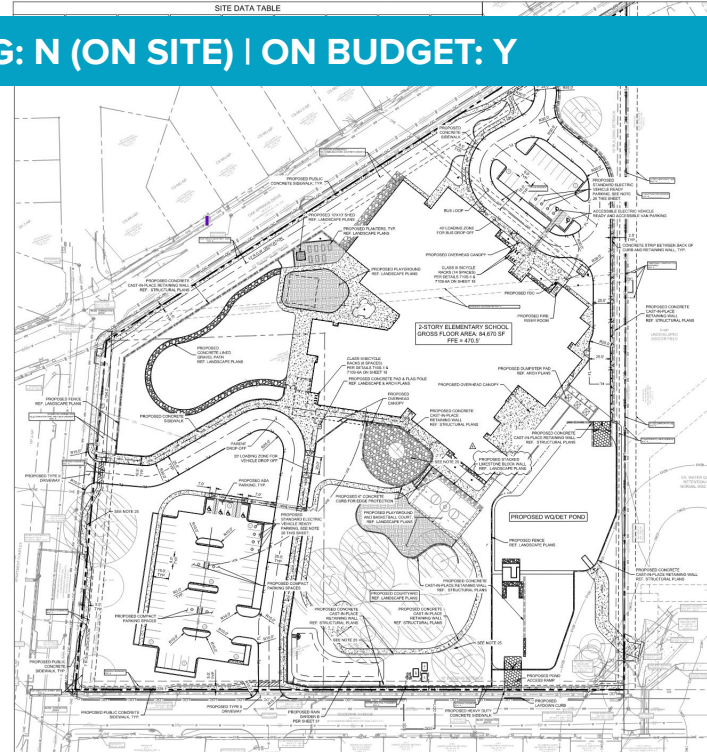

**Conceptual renderings. Final design may vary.*

CBOC Meeting | May 12, 2026

UP NEXT:




BOND
PROGRAM
AUSTIN ISD 2022

Worker Protection & Safety Update

Worker Protections Update

Current sites being monitored:

- Andrews ES, Allison ES, Anderson HS, Burnet MS, Crockett ECHS, Dobie MS, Harris ES, Houston ES, Langford ES, LBJ ECHS, Linder ES, Martin MS, McCallum HS, Navarro ECHS, Northeast ECHS, O. Henry MS, Pecan Springs ES, Sadler Means YWLA, Travis ECHS, and Wooten ES

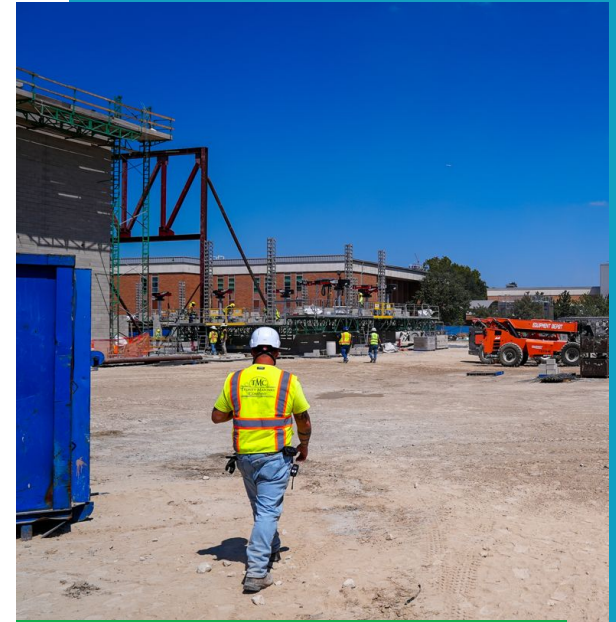

Travis Early College High School

Worker Protections - Safety

	Q4 2025	Total to Date
Interviews Conducted	304	1476
Potential Findings:		
Reported	14	96
Resolved- No Action Necessary	0	60
Resolved - Action Taken	8	22
Pending Further Review	6	14

Q1 2026 Summary

- Water Provisions (3 Findings) These findings involved contractors failing at Travis ECHS, Sadler Means and Burnet MS to provide adequate or easily accessible drinking water for their workers. Actions taken to resolve these included:
 - Deploying accessible potable water stations in the field and submitting photo proof of the setups to the monitors.
 - Formally reminding foremen of OSHA water requirements and establishing an extra backup water supply at the main project trailers.
- **OSHA-10 Certification Issues (5 Findings)** Actions taken to resolve these included:
 - **Certification Completed (1 finding):** The issue was resolved after the worker successfully enrolled in, completed the OSHA-10 course, and provided their certificate.
 - **Worker Removal (4 findings):** The remaining cases were closed because the non-compliant workers were permanently removed from the job sites.

Worker Protections - Wage & Benefits

	Q4 2025	Total to Date
Interviews Conducted	304	1476
Potential Findings:		
Reported	5	57
Resolved - No Action Necessary	2	34
Resolved - Action Taken	0	5
Pending Further Review	3	18

Q1 2026 Summary

- Wage Claim (3 pending - 18 resolved to date. Our auditors did resolve and correct the Linder and Wooten findings with subcontractors, Arrow Glass and Savage Land Solutions. .
- Pending reviews (3) for NECHS, LBJ, Houston are under further review and should be resolved by Q2.

Safety Update

	Q1 2026	Contract to Date (Dec 23 - Mar 26)
Recorded Man-Hours	346K	2.28M
Recordable Incidents	0	7
Student, Staff, Visitor Incidents	0	1

Q1 2026 Safety Summary

- **Exposures:** Total man-hours across all AISD bond projects reached **2,281,390**. This continued high volume of labor demonstrates sustained operational momentum, with project teams successfully maintaining peak safety efficiency during intensive construction phases.
- **Incidents:** The quarter recorded **zero (0) recordable incidents**, making the second consecutive quarter with **no recordables**.

Recordable Incident Analysis & Proactive Actions

- **Zero (0) Recordable Incidents (Q1 2026):** Maintained a Total Recordable Incident Rate (TRIR) of 0.0, successfully mitigating workplace hazards across all active project sites through rigorous safety consultant field oversight.
- **Operator Certification Excellence:** Executed a comprehensive “deep dive” training initiative in March 2026. The training reinforced the **3 Pillars of OSHA Operator Certification** (e.g. Formal Instruction, Practical Training, and Performance Evaluation) across all equipment categories including cranes, forklifts, and aerial lifts to ensure compliance with OSHA 1910.178 and 1926.1427.

Student, Staff, Visitor Incident Analysis & Corrective Actions

- **Campus & Community Safety:** Achieved **zero (0)** incidents involving students, staff, or visitors for the second consecutive quarter. This milestone was sustained through strict site-perimeter integrity, clear signage, and coordinated logistics to ensure zero interface between construction activities and school operations.

UP NEXT:










**BOND
PROGRAM**
AUSTIN ISD 2022

2022 BOND TARGETED PROJECTS


2022 Project Status Overview

Completed numbers of targeted projects across campus facilities with the following scopes of work:


	Secure Vestibules: 64 of 64 completed
	MEP Renovations: 7 of 56 completed
	Fencing: 56 of 62 completed
	Security Film: 99 of 99 completed
	Mental Health Centers: 2 of 35 completed
	Community Centers/Food Pantries: 0 of 5 completed
	Pre-K Improvements: 2 of 12 completed

Safety Projects

Prop A.

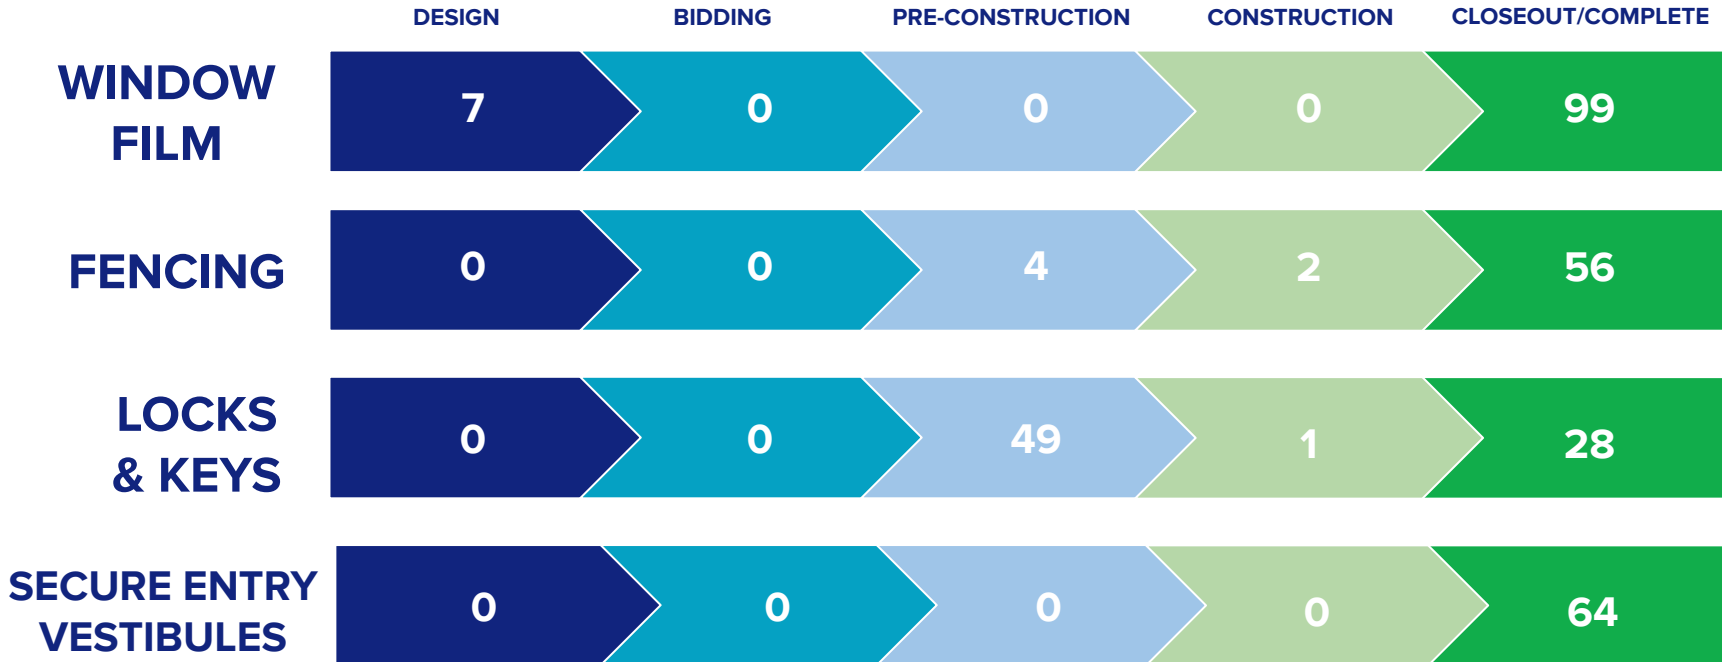

Kealing Middle School



Scan the QR code to see the campus project page [Project Fact Sheet](#)



Pending scope approval, construction is tentatively anticipated to begin in June 2026.

Turf & Field Project Updates

Campus	Track & Turf Open	Lights	Field Events	Bleachers	Press Box	Substantial Completion
LBJ ECHS	12/15/26 <i>(In Use by Campus only)</i>	5/15/26 <i>(Pending AE)</i>	In Use	8/20/26	9/30/26	10/5/26
Austin HS	1/12/26 <i>(In Use by Campus only)</i>	7/15/26 <i>(Pending AE)</i>	In Use	8/20/26	9/30/26	10/5/26
Bowie HS	2/11/26 <i>(In Use by Campus only)</i>	6/30/26	In Use	8/20/26	9/30/26	10/5/26
LASA	2/25/26 <i>(In Use by Campus only)</i>	5/31/26	5/31/26	8/20/26	9/30/26	10/5/26

- All future dates are anticipated, but subject to change if there are unforeseen circumstances
- Public use of the turf project is dependent upon issuance of a CO/TCO by the City of Austin, which will occur only after completion of all outstanding project elements.

Turf & Field Project Updates

Campus	Track & Turf Open	Lights	Field Events	Bleachers	Press Box	Substantial Completion
Akins ECHS	4/27/26 <i>(In Use by Campus only)</i>	6/30/26	5/31/26	8/20/26	9/30/26	10/5/26
McCallum HS	5/4/26 <i>(In Use by Campus only)</i> Track: 5/31/26	8/8/26	5/31/26	8/20/26	9/30/26	10/5/26
Navarro ECHS	4/27/26 <i>(In Use by Campus only)</i>	6/30/26	5/31/26	8/20/26	9/30/26	10/5/26
Northeast ECHS	5/12/26	5/25/26	5/25/26	8/20/26	9/30/26	10/5/26

- All future dates are anticipated, but subject to change if there are unforeseen circumstances
- Public use of the turf project is dependent upon issuance of a CO/TCO by the City of Austin, which will occur only after completion of all outstanding project elements.

UP NEXT:




**BOND
PROGRAM**
AUSTIN ISD 2022

*i love Books
SO much*

2017 BOND PROJECTS

2017 Bond Projects

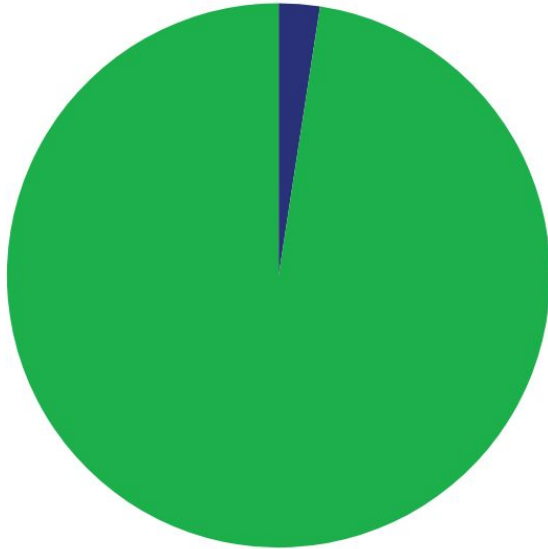

■ 2017 Bond Projects Completed (163)

■ 2017 Bond Projects Underway (7)

- House Park
- Gus Garcia MS
- Eastside ECHS
- General Marshall MS
- Anderson HS
- Paredes MS
- Blazier ES

*Please See File: [2017 Bond Projects](#)

2017 Bond - Eastside Early College High School



Scan the QR code to see the campus project page [Project Fact Sheet](#)

- AFD passed the Fire Final Inspection on 11/12.
- Deferred submittals approved on 3/26.
- The GC is working on scheduling repairs in response to COA SSI (Site & Subdivision Inspection).
- Discussions continue with CMD, BPS, and Legal Counsel to determine the next steps toward a resolution for the Wellness Walk.



UP NEXT:



**BOND
PROGRAM**
AUSTIN ISD 2022

CBOC Committee Operations

Committee Operations

- Survey Update
- Bylaws Revisions Update
- SPED Camera Board Response



Harris Elementary School

SPED Camera Board Response

CBOC Question: Has a final resolution been reached regarding pre-wiring versus case-by-case installation of SPED camera infrastructure? Yes.

Board of Trustees Meeting (March 26, 2026):

- [RECORDING:](#) 1:06:35-1:15:55
 - Superintendent Segura confirmed:
 - Funding for cameras was included during bond planning
 - Available funds **do not support district wide pre-wiring (including cabling)**
 - He **does not support a full pre-wiring approach**
 - Trustee De Urioste acknowledged that:
 - The current process is **the most efficient approach**
 - Dr. Cherry Lee shared SPED camera implementation data:
 - **SY 25-26:** 12 requests (11 approved & 1 denied)
 - **SY 24-25:** 14 request (all approved)
 - **SY 23-24:** 15 requested (all approved)
 - All deadlines for SPED camera installation have been met

ADJOURN



THANK YOU!



BOND
PROGRAM
AUSTIN ISD 2022

GLOSSARY OF TERMS

